

ADDENDA COVER PAGE

The following Addenda have been currently released for this project, and are attached to this cover page:

- Addendum #1-08/20/2021

Please stay tuned for additional Addenda, if any, for this project. This cover sheet will reflect additional Addenda and the attachments to this cover page will include any and all current Addenda as they are published.

ADDENDUM # 1

TO THE RFQ FOR:

Dardenne Greenway Connector Project

City of O'Fallon, Missouri

100 North Main Street

O'Fallon, Missouri 63366

City of O'Fallon, Missouri

100 North Main Street

O'Fallon, MO 63366

636-379-5590

636-978-4144 Fax

E-mail: cclercx@ofallon.mo.us

August 20, 2021

INFORMATION


The information attached to this document will supplement the original RFQ solicitation:

1. Supplemental Information:

- a. TAP application general layout and location map
- b. TAP application project development schedule

END OF ADDENDUM

EXHIBIT A.1 Dardenne Greenway Improvements: Technology Dr Trailhead Connections

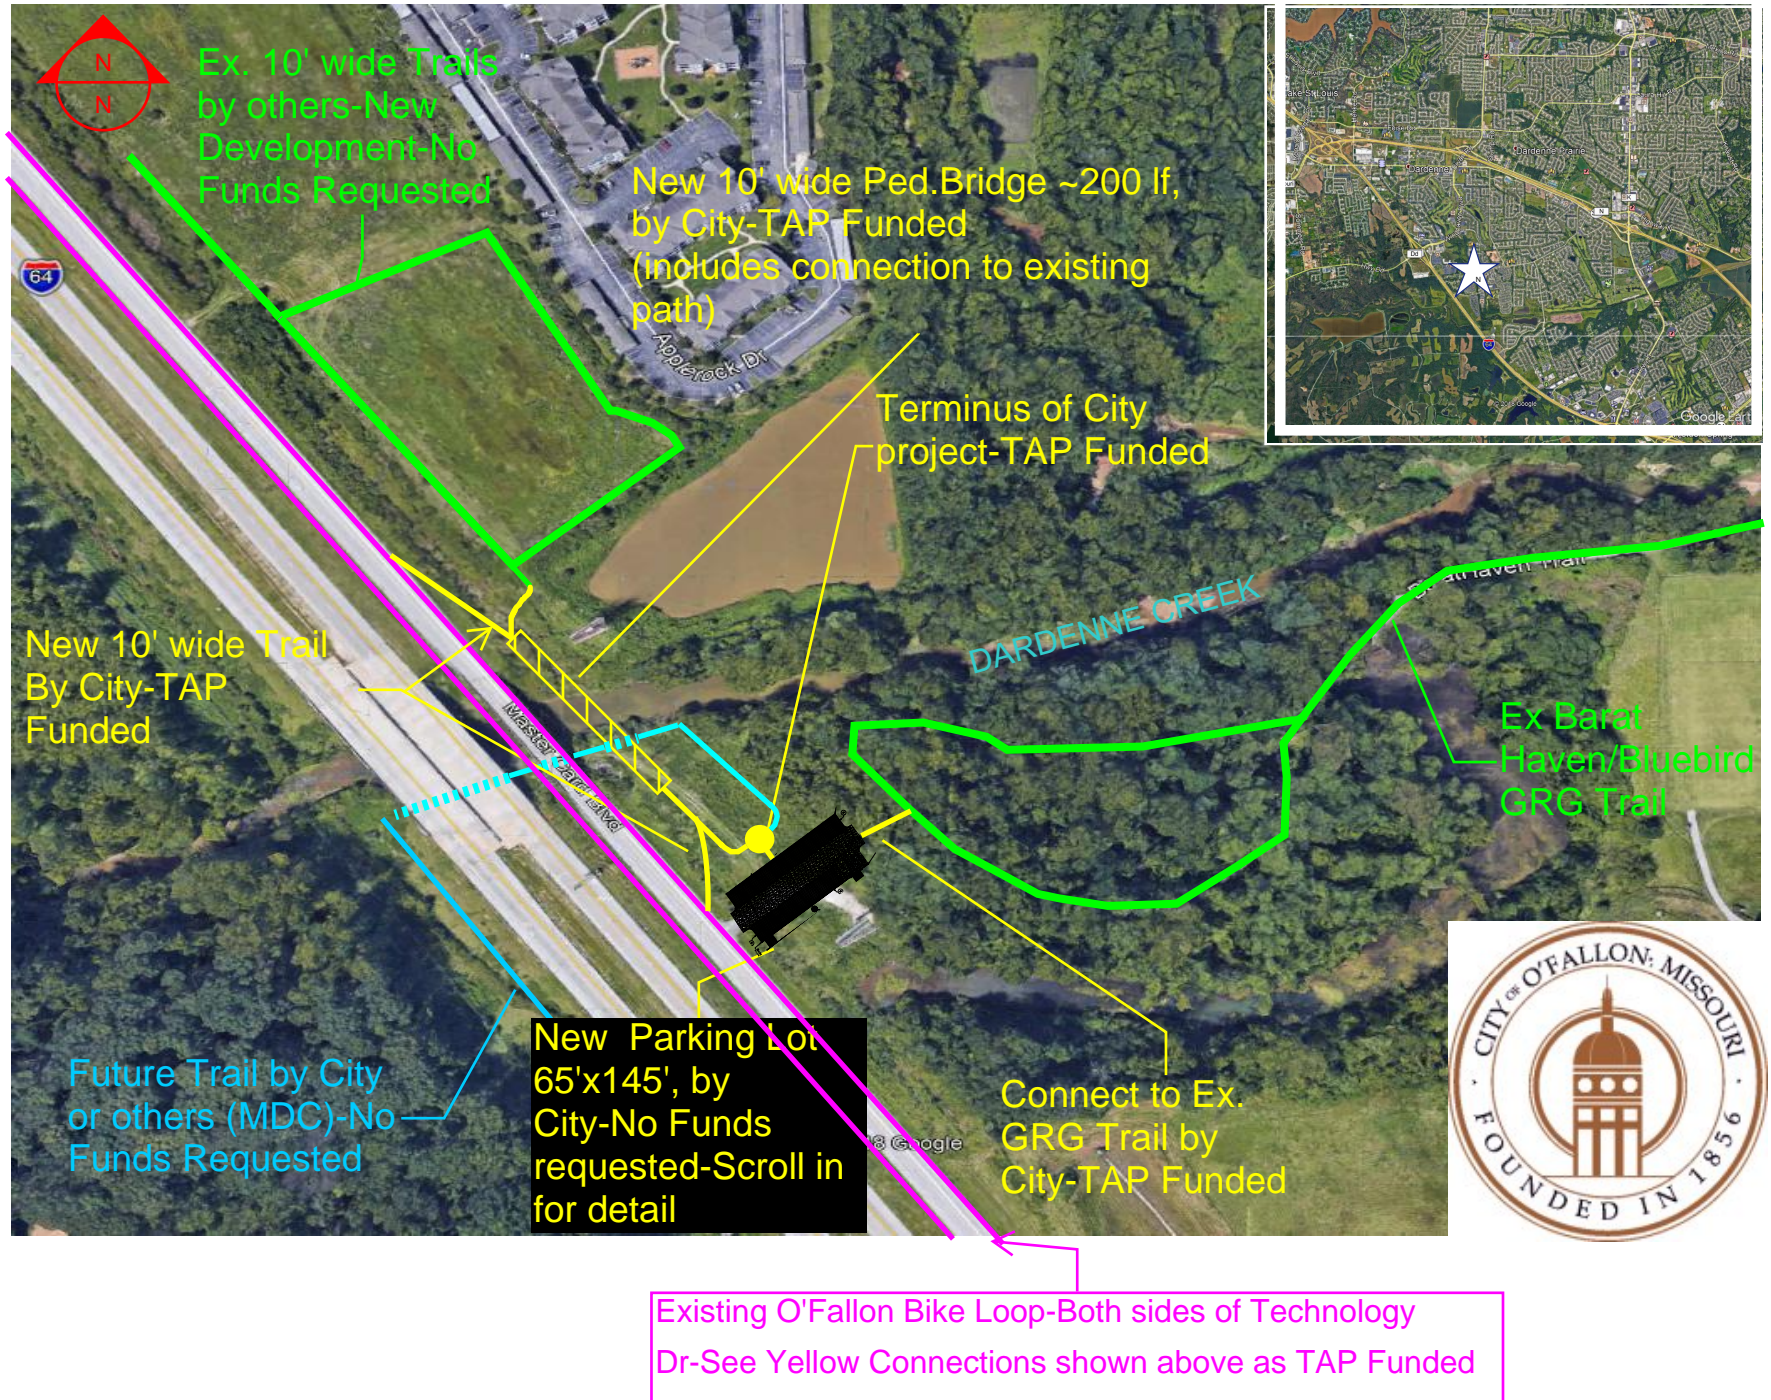

PROJECT DEVELOPMENT SCHEDULE

Note: *many stages can occur concurrently.*

Activity Description	Start Date (MM/YYYY)	Finish Date (MM/YYYY)	Time Frame (Months)
Receive notification letter	04/2021	04/2021	1
Execute agreement (project sponsor and DOT)	05/2021	06/2021	2
Engineering services contract submitted and approved*	07/2021	11/2021	5
Obtain environmental clearances (106, CE2, T&E, etc.)	10/2021	11/2021	2
Public meeting/hearing	12/2021	12/2021	1
Develop and submit preliminary plans	10/2021	12/2021	3
Preliminary plans approved	12/2021	01/2022	2
Develop and submit right-of-way plans	11/2021	12/2021	2
Review and approval of right-of-way plans	01/2022	02/2022	2
Submit and receive approval for notice to proceed for right-of-way acquisition (A-Date)*	02/2022	03/2022	2
Right-of-way acquisition	03/2022	10/2022	8
Utility coordination	10/2021	12/2023	27
Develop and submit PS&E	11/2022	12/2022	2
District approval of PS&E/advertise for bids*	01/2023	02/2023	2
Submit and receive bids for review and approval	03/2023	05/2023	3
Project implementation/construction	06/2023	06/2024	12
* Finish date must match fiscal year for each milestone shown in bold text.			
